Los Angeles Harbor College

03H - *Active Summary Layout by Phase

Data Date - 01-Oct-14

Activity ID	Activity Name	Duration % Complete	Start	Finish
307	Theater Drama Speech Building	91.42%	11-Jul-02 A	31-Dec-15
329	Old Administration Modernization	70.21%	31-May-07 A	25-Dec-17
338.01	Campus Wide ADA Transition	60.56%	15-Mar-10 A	23-Nov-17
344	Science Complex	94.63%	09-Dec-02 A	02-Jun-15
348	Learning Resource Center	76.41%	01-May-06 A	01-Aug-17
350.01	S.A.I.L.S. Student Union	62.96%	30-Nov-09 A	20-Nov-17
350.02	S.A.I.L.S. Astronomy Modernization	89.95%	30-Nov-09 A	15-Apr-15
350.03	S.A.I.L.S. Infrastructure/Land/Hardscape/Security	74.78%	01-Oct-09 A	25-Apr-18
363	West Parking Structure	100%	10-Mar-08 A	15-Aug-14 A
366.03	Campus Marque Modernization	83.82%	02-Feb-09 A	19-Feb-16
366.04	NEA/SS Enhancement	100%	02-Feb-09 A	15-Aug-14 A
366.09	Campus Restrooms	100%	03-Nov-09 A	14-Apr-14 A

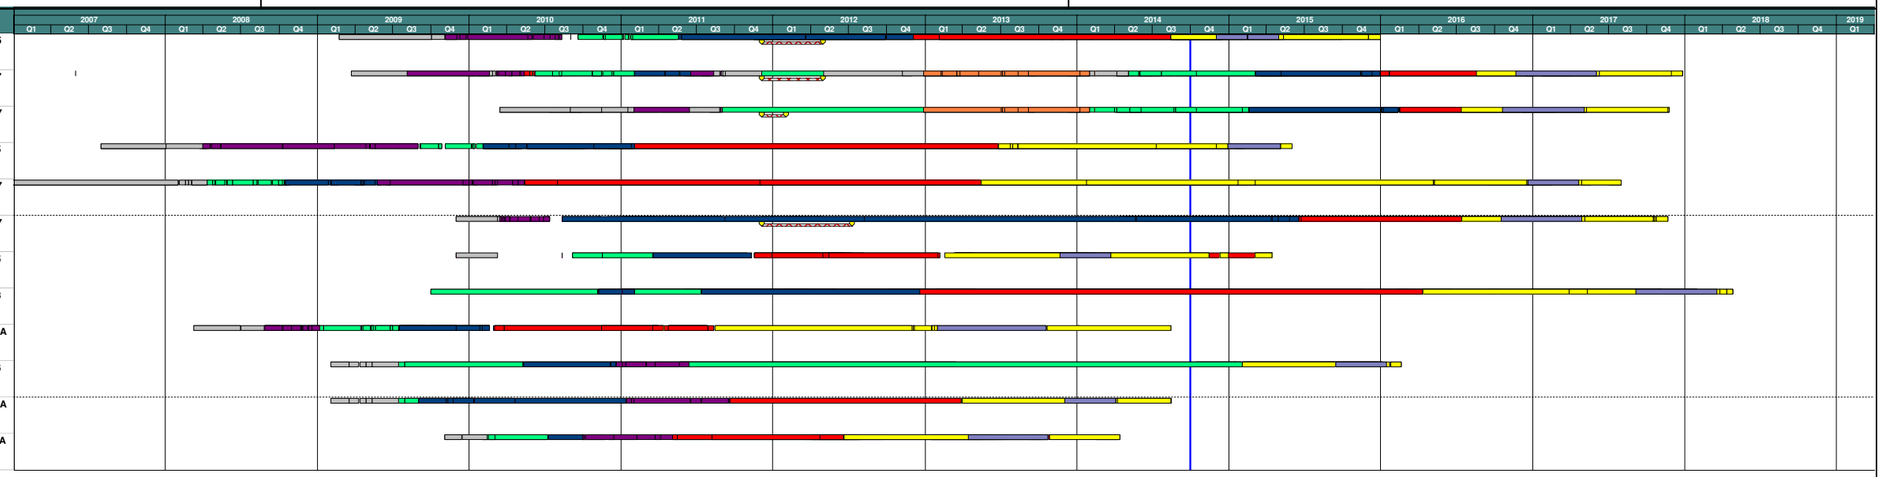

MORATORIUM 2 | DB Procur | DSA | Construction
Programming | Design | Bid/Award | Close-out

TASK filters: 03H - Active Projects, Cash Flow - Not Equal to Act ID.

© Oracle Corporation
